

THE CITY OF NAPOLEON

BUILDING & ZONING DEPARTMENT

255 W. RIVERVIEW

(419)592-4010

Sidewalk/Curb Replacement Permit

Permit Number: SW2006-3

Page 1 of 1

Printed: 5/4/2006

Property Address: 325 Carey St.

Applicant

Address: Jesusa Gonzalez
325 Carey St.
Napoleon, OH 43545

Approval Date: 5/4/2006

Phone: 419-592-0404

Owners

Name: Jesusa Gonzalez
325 Carey St.
Napoleon, OH 43545

Phone: 419-592-0404

Contractors

Fees and Receipts:

Number	Description	Amount
FEE2006-343	Sidewalk/Curb	\$25.00
Total Fees:		\$25.00
RCPT2006-169		\$25.00

Description of work to be done:

Sidewalk replacement



Applicant signature: _____ Date: _____

pd
26250
11/21/06

SW06-3

CITY OF NAPOLEON GENERAL PERMIT APPLICATION

THIS APPLICATION IS FOR RESIDENTIAL CONSTRUCTION INCLUDING BUILDING, ELECTRICAL, PLUMBING MECHANICAL, DEMOLITIONS, REMODELING.

DATE: 5-4-06 JOB LOCATION: 325 Carey St.

OWNER: Jesusa Gonzalez PHONE: 419-592-0404

OWNER ADDRESS: 325 Carey St. CITY: Napoleon ZIP: 43845

CONTRACTOR: Self

PHONE #: _____ CELL PHONE# _____

CONTRACTOR LICENSED WITH THE CITY OF NAPOLEON?: YES NO:

Is any of the above job going to be subcontracted out? Yes No:

If yes to whom: _____

DESCRIPTION OF WORK TO BE PERFORMED: _____

ESTIMATED COMPLETION DATE: _____

PLEASE MARK THE TYPE OF WORK YOU WILL BE PERFORMING

- | | |
|---|--|
| <input type="checkbox"/> A/C ADD ON | <input type="checkbox"/> REMODELING |
| <input type="checkbox"/> BOILER REPLACEMENT | <input type="checkbox"/> ROOFING |
| <input type="checkbox"/> CURBING | <input type="checkbox"/> SEWER REPAIRS** |
| <input type="checkbox"/> DECKS * | <input checked="" type="checkbox"/> SIDEWALK* |
| <input type="checkbox"/> DRIVEWAY* | <input type="checkbox"/> SIDING |
| <input type="checkbox"/> ELECTRICAL SERVICE UPGRADE | <input type="checkbox"/> STORAGE SHED* |
| <input type="checkbox"/> ELECTRICAL SERVICE NEW | <input type="checkbox"/> SWIMMING POOL* |
| <input type="checkbox"/> FENCE* | <input type="checkbox"/> FURNACE REPLACEMENT |
| <input type="checkbox"/> ADDITIONS* | <input type="checkbox"/> TEMP ELECTRIC |
| <input type="checkbox"/> FURNACE NEW | <input type="checkbox"/> WATER TAP (size _____") |
| <input type="checkbox"/> LAWN METER | <input type="checkbox"/> WINDOWS |
| <input type="checkbox"/> PLUMBING | <input type="checkbox"/> ZONING |

*PLEASE INCLUDE A PICTURE SHOWING MEASUREMENTS FROM EXISTING STRUCTURES AND PROPERTY LINES. INDICATING THE TYPE OF WORK YOU WISH TO PERFORM.

** IF WORK REQUIRES GOING INTO THE STREET A STREET BOND IS REQUIRED!

FOR PERMIT COSTS PLEASE FILL OUT REVERSE SIDE

PERMIT COST WORKSHEET

JOB	BASE FEE	TOTAL
SIDING (only) TOTAL SQ _____ X 1.00 +	\$5.00 =	\$ _____
ROOFING (only) TOTAL SQ _____ X 1.00 +	\$5.00 =	\$ _____
WINDOWS (only) # OF WINDOWS ____ X 1.00 +	\$5.00 =	\$ _____
ELECTRICAL # OF CIRCUITS _____ X 3.00 +	\$15.00 =	\$ _____
ELECTRICAL SERVICE UPGRADE	\$15.00 =	\$ _____
PLUMBING (INSIDE) repairs only	\$10.00 =	\$ _____
PLUMBING/SEWER (OUTSIDE)	\$25.00 =	\$ _____
WATER HEATER	\$5.00	\$ _____
SHED UNDER 200 SQ FT	\$ 5.00	\$ _____
FURNACE OR A/C (REPLACEMENT)	\$ 5.00	\$ _____
DEMOLITION (only)	\$30.00	\$ _____
SIDEWALK REPLACEMENT/ NEW	\$25.00	\$ _____
DRIVEWAY	\$25.00	\$ _____

ALL CONSTRUCTION, ALTERATIONS, REMODELING, SHEDS, DECKS & FENCES NOT LISTED ABOVE IS BASED ON COST OF WORK BEING PERFORMED.

COST OF WORK \$ _____ (SEE CHART) \$ _____

0.00	-	250.00	0.00	11,000.00	-	11,999.00	25.00
250.00	-	1,000.00	10.00	12,000.00	-	12,999.00	26.00
1,000.00	-	1,999.00	12.00	13,000.00	-	13,999.00	27.00
2,000.00	-	2,999.00	14.00	14,000.00	-	14,999.00	28.00
3,000.00	-	3,999.00	16.00	15,000.00	-	15,999.00	29.00
4,000.00	-	4,999.00	18.00	16,000.00	-	16,999.00	30.00
5,000.00	-	5,999.00	19.00	17,000.00	-	17,999.00	31.00
6,000.00	-	6,999.00	20.00	18,000.00	-	18,999.00	32.00
7,000.00	-	7,999.00	21.00	19,000.00	-	19,999.00	33.00
8,000.00	-	8,999.00	22.00	20,000.00	-	20,999.00	34.00
9,000.00	-	9,999.00	23.00	21,000.00	-	21,999.00	35.00
10,000.00	-	10,999.00	24.00	22,000.00	-	22,999.00	36.00
				Over 22,999		Please Call	

City of Napoleon


Residential Sidewalk Specifications

I. Work Included


- A. Under this item the Contractor shall improve by construction, reconstruction or repairing as is necessary, public sidewalks between limits established by the Engineer.
- B. Sidewalks shall be at least four (4) inches in thickness and, in driveway crossings and within five (5) feet there of, six (6) inches in thickness. When sidewalks abut with the curb, the width shall be five (5) feet or as wide as the existing sidewalks; in either case, a minimum width of four (4) feet shall be required. Edge of walks parallel with the street shall be placed at least one (1) foot from the property line or meet existing sidewalks. The Engineering Department will give line and grade.
- C. Old concrete sidewalk material shall be removed and granular material used for fill if necessary, to meet grade.
- D. All work shall conform to the standard specifications published by the Ohio Department of Transportation (O.D.O.T.) and the City, in effect at the date of contract and the requirements under these specifications.
 1. Referenced O.D.O.T. specifications as follows:
 - 608. Concrete Walks
 - 499. Concrete
 - 511.15 Depositing and Curing Concrete in Cold Weather

II. Materials and Finish:

- A. A minimum of four (4) inches of ODOT item 304 or 411 crushed limestone base shall be provided and compacted in place.
- B. The concrete mix shall be ODOT Class C mix with 5 to 6% air entrainment. All surface area shall be broom finished and sealed with an Engineer approved concrete sealer. All joints shall be trowel-cut with a maximum joint spacing of 5 feet. The depth of cut shall be a minimum $\frac{1}{4}$ of the thickness of the slab. Expansion joints shall be placed at a maximum of 40 feet and at all intersecting walks.

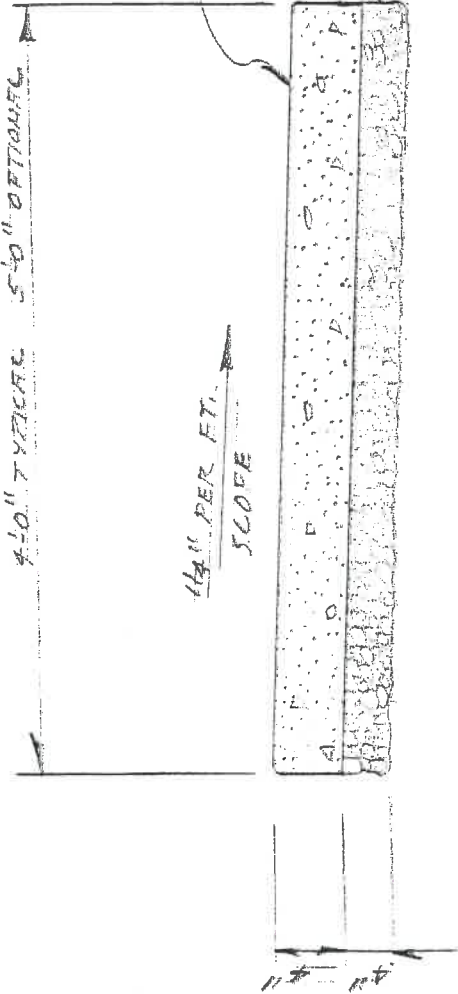

SIDEWALK SECTION

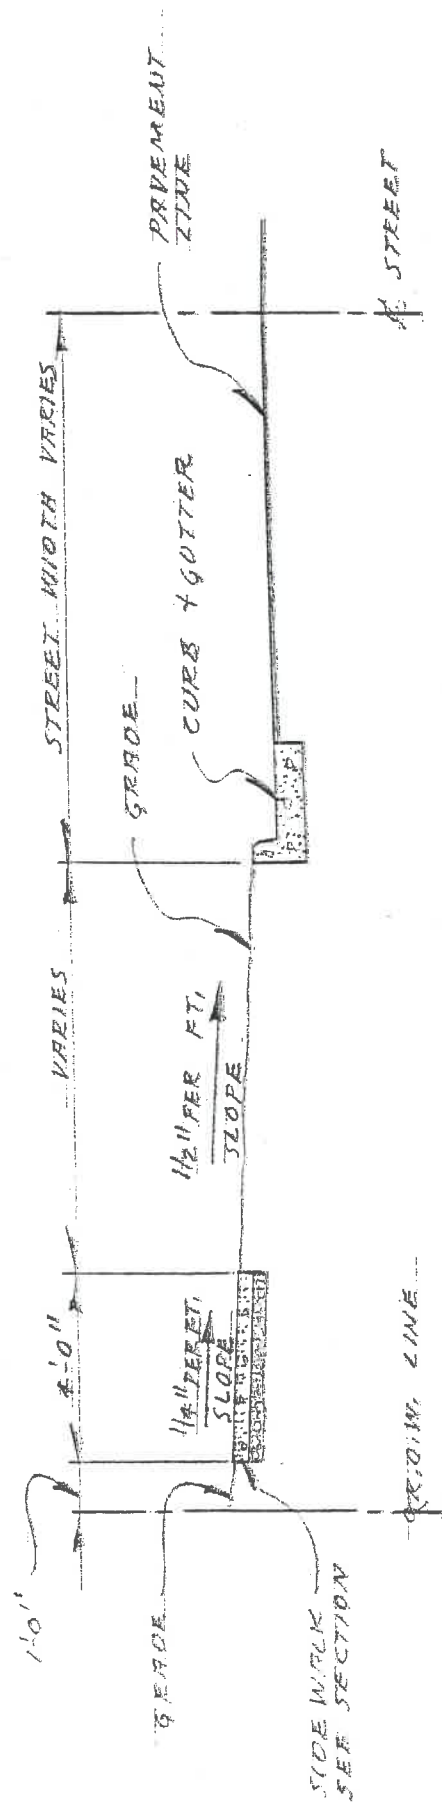

SIDEWALK LINE & ELEVATION DET.

Jesusa A. Gonzalez

Phone: 419-34-2939

325 Carey Street

Napoleon, OH 43545

November 10, 2006

To Whom It May Concern:

I needed to pay for labor as well as buy the materials. Therefore, I paid Jaime Herrera \$250.00 at the time that the concrete was poured.

Thank you,



Jesusa A. Gonzalez

CENTRAL DISPATCH
419/841-3435



7901 Sylvania Ave. • Sylvania, Ohio 43560

Dispatch Ticket # 73021818 Order# 48

	LEAVE JOB
10:00	ARRIVE JOB
	UNLOAD TIME

NVOICE TO SALE-GONZALO GO

DELIVER TO N. SCOTT NEAR RAILROAD TRK
OFF N. SCOTT NEAR RAILROAD TRK
DKS

WATER ADDED AT JOB SITE
OTHER ADDED AT JOB SITE
GALS.

	RETURN PLANT
9:50	LEAVE PLANT
	TOTAL TRIP TIME

GONZALO 419-592-

DATE	QUANTITY	ORDERED	DELIVERED	JOB	MIX	TRUCK	PLANT	TIME LOADED
11/08/89	2.00	2.00				0033	13	09:14:01

CONDITIONS

The undersigned hereby agree to the following conditions of sale and delivery. That he/she is a duly authorized representative of the above customer or accepts personal liability for same. The undersigned directs and grants permission to All Ohio Ready Mix Concrete to deliver concrete on the above premises, assumes all responsibility and does hereby release All Ohio Ready Mix Concrete from any liability. The undersigned agrees that a warning of potential damage has been made by All Ohio Ready Mix Concrete, and will hold All Ohio Ready Mix Concrete harmless from any loss suffered, either directly or indirectly, by the trucks presence or passage. Due to circumstances beyond the control of All Ohio Ready Mix Concrete, All Ohio Ready Mix Concrete will be unable to warrant or guarantee concrete placed during, or exposed to, severe weather conditions not conducive to proper concrete placement practices in accordance with ASTM. The undersigned assumes all responsibilities pertaining to correct procedures and practices. All warranties either expressed or implied are void if additions to the concrete at the site exceed mix design specifications (including maximum water limit), or if the concrete has been on the truck for more than (90) minutes from the time stamped in the box marked "Time Loaded".

DELIVER EVALUATION

	Good	Fair	Poor
Ability	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
Attitude	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
Overall Performance	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
Comments			

QUANTITY	UNIT PRICE	TOTAL
2.00	5.25	10.50
2.00	5.00	10.00
		7089

CUSTOMER SIGNATURE

SUB-TOTAL

SALES TAX

TOTAL

Signature acknowledges receipt of materials, acceptance of conditions and reverse side communications standard. I agree to pay the amount shown above according to my credit card agreement.

CAUTION: Cement Contains Chemicals that may be harmful to skin.

TRUCK	LOAD SIZE	DESIGN DTY	REQUIRED	BATCHED	VAR	MOISTURE	ACTUAL WAT
8033	2.00 YD	1895.0 lb	3434.0 lb	3400.0 lb	-34.00	1.300% M	5.23 gl
		1800.0 lb	2749.3 lb	2840.0 lb	90.70	5.744% A	18.49 gl
		200.00 lb	1200.0 lb	1200.0 lb	0.00		
		1.25 YD	15.00 oz	15.00 oz	0.00		
		26.00 gl	38.82 gl	39.00 gl	0.18		39.00 gl
NON-SIMULATED		NUM BATCHES: 1		WATER/CEMENT: 0.500		DESIGN WATER: 72.0 gl	
LEAD TOTAL: 766 lb		DESIGN W/C: 0.500		WATER/CEMENT: 0.500		DESIGN WATER: 72.0 gl	
SLUMP: 4.00		WATER IN TRUCK: 10.0 gl		ADJUST WATER: 0.0 gl / load		ACTUAL WASH: 62.7 gl	

73-000130

TIME: 08:38

10 LB



7901 Sylvania Ave. • Sylvania, Ohio 43560

Dispatch Ticket # 73021818 Order# 48

INVOICE TO SALE--GONZALO GO	DELIVERY TO Y NAPOLEON	WATER ADDED AT JOB SITE
GONZALO 419-592-	OFF N. SCOTT NEAR RAILROAD TRK	OTHER ADDED AT JOB SITE
		GALS.

	LEAVE JOB
12:00	ARRIVE JOB
	UNLOAD TIME
	RETURN PLANT
9:50	LEAVE PLANT
	TOTAL TRIP TIME

DATE	QUANTITY	ORDERED	DELIVERED	JOB	MIX	TRUCK	PLANT	TIME LOADED
11/02/06	2.00	2.00	2.00	48	5106D041	0033	73	09:34AM

CONDITIONS	DRIVER EVALUATION	QUANTITY	UNIT PRICE	TOTAL	
<p>The undersigned hereby agree to the following conditions of sale and delivery. That he/she is a duly authorized representative of the above customer or accepts personal liability for same. The undersigned directs and grants permission to All Ohio Ready Mix Concrete to deliver concrete on the above premises, assumes all responsibility and does hereby release All Ohio Ready Mix Concrete from any liability. The undersigned agrees that a warning of potential damage has been made by All Ohio Ready Mix Concrete, and will hold All Ohio Ready Mix Concrete harmless from any loss suffered, either directly or indirectly, by the trucks presence or passage. Due to circumstances beyond the control of All Ohio Ready Mix Concrete, All Ohio Ready Mix Concrete will be unable to warrant or guarantee concrete placed during, or exposed to, severe weather conditions not conducive to proper concrete placement practices in accordance with ASTM. The undersigned assumes all responsibilities pertaining to correct procedures and practices. All warranties either expressed or implied are void if additions to the concrete at the site exceed mix design specifications (including maximum water limit), or if the concrete has been on the truck for more than (90) minutes from the time stamped in the box marked "Time Loaded".</p>	<p>Good 1 Poor</p> <p>Fiber <input type="checkbox"/> <input type="checkbox"/> <input type="checkbox"/> <input type="checkbox"/></p> <p>Short Load Charge <input type="checkbox"/> <input type="checkbox"/> <input type="checkbox"/> <input type="checkbox"/></p> <p>Attitude <input type="checkbox"/> <input type="checkbox"/> <input type="checkbox"/> <input type="checkbox"/></p> <p>Overall Performance <input type="checkbox"/> <input type="checkbox"/> <input type="checkbox"/> <input type="checkbox"/></p> <p>Comments _____</p>	2.00	90.85	181.70	
		2.00	5.00	10.00	
	CUSTOMER SIGNATURE				
	<p>Signature acknowledges receipt of materials, acceptance of conditions and reverse side hazard communications standard. I agree to pay the amount shown above according to my credit card agreement.</p> <p>CAUTION: Cement Contains Chemicals that may be harmful to skin.</p>				
				SUB-TOTAL	
				SALES-TAX	
				TOTAL	

TRUCK	USER LOGIN	DISP TICKET NUM	TICKET NUM	TICKET ID	TIME	DATE						
0033	USER	73021818	3928	4102	09:29	11/02/2006						
LOAD SIZE	MIX CODE				SEQ	73-000130						
2.00 yd	5106D041				D	1505						
MATERIAL	DESIGN	QTY	REQUIRED	BATCHED	VAR	%MOISTURE	ACTUAL WAT					
E15-57'S	1695.0	lb	3434.0	lb	3400.0	lb	-34.00	1.300% M	5.23	gl		
171-2NS	1300.0	lb	2749.3	lb	2840.0	lb	+ 90.70	5.744% A	18.49	gl		
TYPE-1	600.00	lb	1200.0	lb	1200.0	lb	0.00					
MICROAIR	1.25	/C	15.00	oz	15.00	oz	0.00					
WATER	36.00	gl	38.82	gl	39.00	gl	0.18					
NON-SIMULATED	NUM BATCHES:	1								39.00	gl	
LOAD TOTAL:	7766	lb	DESIGN W/C:	0.501	WATER/CEMENT:	0.506A	DESIGN WATER:	72.0	gl	ACTUAL WATER:	62.7	gl
SLUMP:	4.00	"	WATER IN TRUCK:	10.0	gl	ADJUST WATER:	0.0	gl	/load			

LOAD COMPLETED LOAD TIME: 08:38 TARES: _____
 AGG SCALE B:1 S: 20 LB E: 20 LB CEM SCALE B:1 S: -5 LB E: 10 LB

