


653 W. Clinton

SCANNED

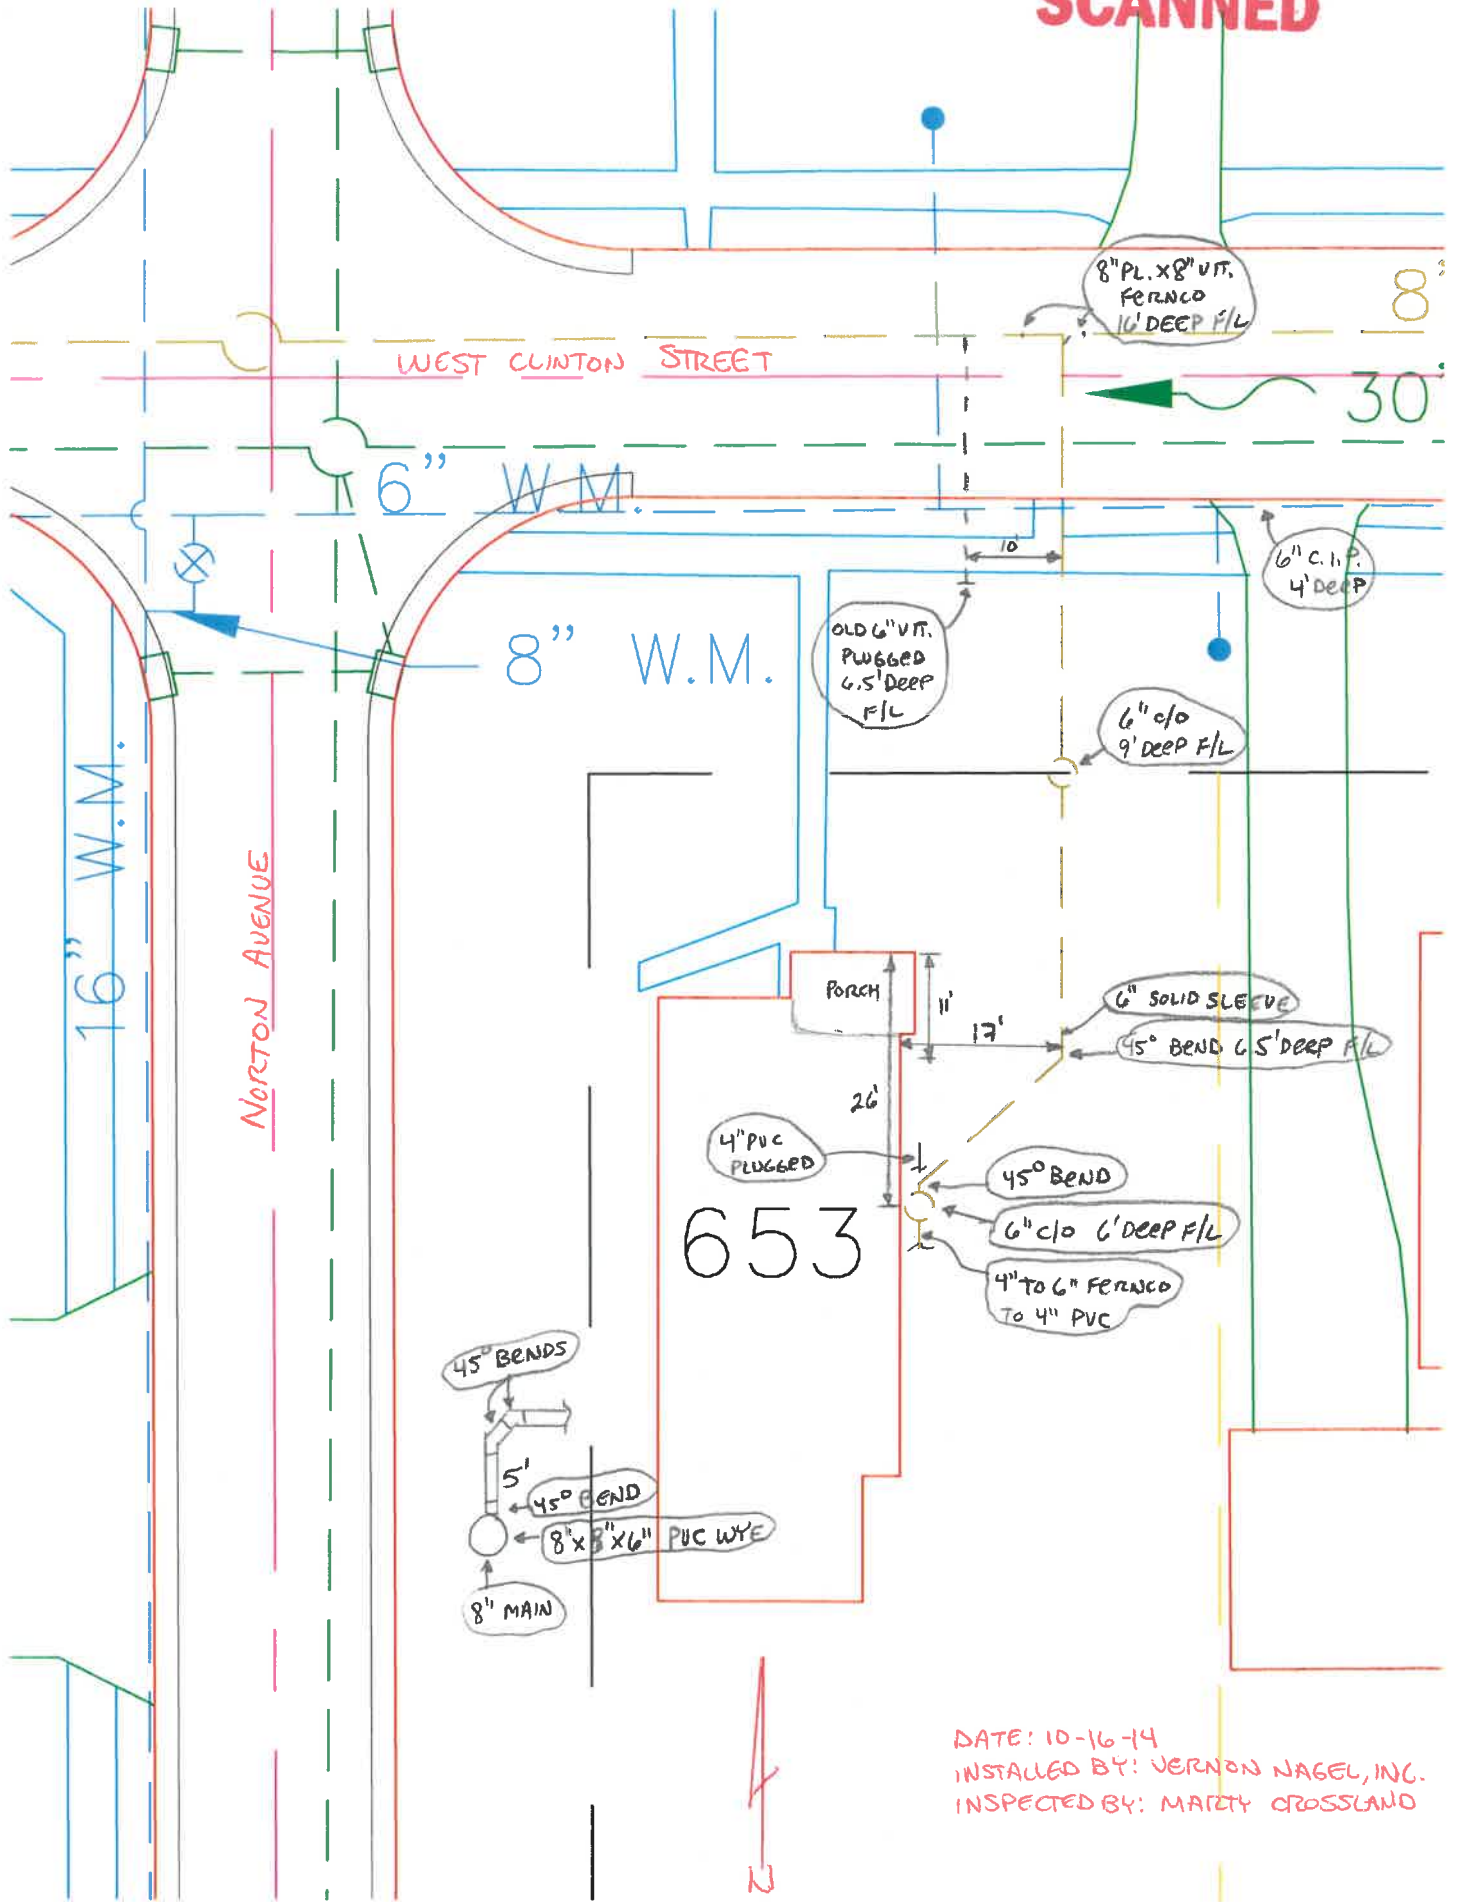

10-16-14

653 W. CLINTON SANITARY TAP

7:00 AM - 4:30 PM

9.5 HR

JACK - FOREMAN

HARRY - OPERATOR - 330C EXCAVATOR

KEVIN - OPERATOR - 930K LOADER

BUZZ - LABORER

2 - FINLEY TRUCKS

MHE - NAGEL TRUCK

MATERIALS:

6.5 LF 8" SDR 35 PVC PIPE

1 - 8" x 8" x 6" PVC BTEE

2 - 8" VIT TO 8" PL. FERRO

3 2 - 45° BEND (6")

52 LF 6" SDR 35 PVC PIPE

1 - 6" C/O W/ CAP

1 - 6" PVC PLUG

10-17-14 NOON - 3PM

3 HR

EXCAVATE ROAD FOR CONC. BASE + ASPHALT SURFACE


JACK - FOREMAN

HARRY - OPERATOR - 320D EXCAVATOR

KEVIN - OPERATOR - 930K LOADER

BUZZ - LABORER

7.5 CY FS CONCRETE BASE

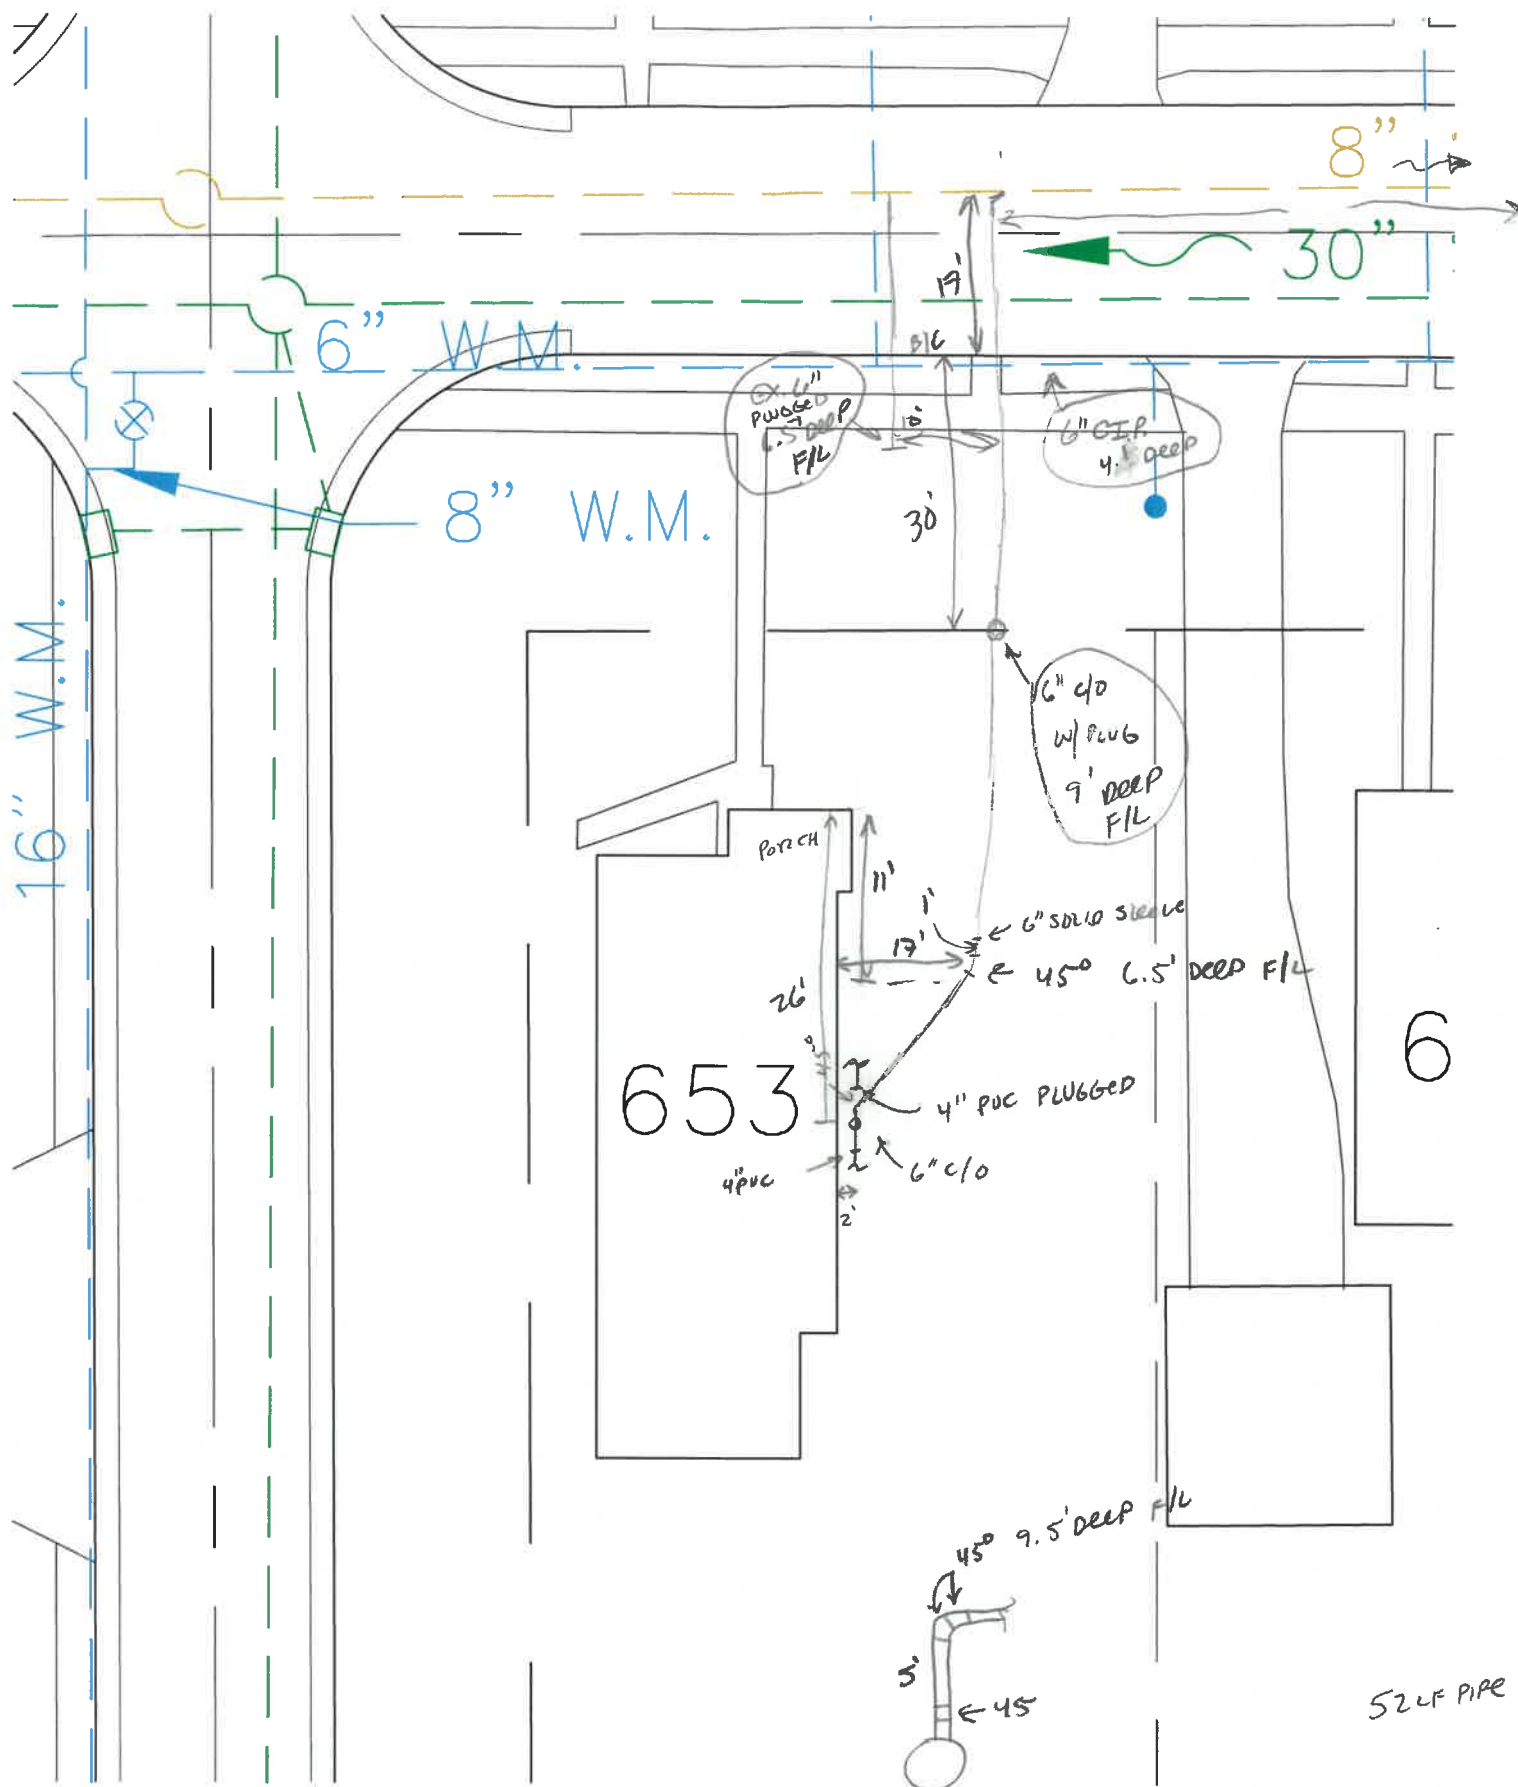

16" W.M.

6" W.M.

8" W.M.

653

6

EX 6" PUGHED
6.5' DEEP
FIL

6" CIP
4' DEEP

6" C/D
W/ PUGH
9' DEEP
FIL

6" SOLID SILEX
45° 6.5' DEEP FIL

4" PVC PLUGGED

45° 9.5' DEEP FIL

52 LF PIPE





Pettisville • Stony Ridge • McClure

M&R REDI-MIX, INC.

READY MIXED CONCRETE • AGGREGATE
SUPPLIES • CUSTOM TRUCKING
(800) 786-6325

521 Commercial Street
Pettisville, OH 43553
PH: (419) 445-7771

5601 Cherry Street
Stony Ridge, OH 43463
PH: (800) 786-6325

L-207 Rd. 1-C
McClure, OH 43534
PH: (419) 746-8442

MAILING ADDRESS
BOX 53038
PETTISVILLE, OHIO 43553

CAUTION

May cause eye or skin injury. Contains Portland cement. Freshly mixed cement, mortar, concrete, or grout may cause skin injury.

TAKE THESE PRECAUTIONS:

1. Avoid all contact with eyes.
2. Wear rubber boots and gloves, and avoid prolonged contact directly with skin or through porous materials.
3. In case of contact with skin or eyes. FLUSH THOROUGHLY WITH WATER.
4. If irritation persists, get medical attention promptly.
5. Keep children away.

LEAVE PLANT	ARRIVE JOB	START POUR
FINISH POUR	LEAVE JOB	ARRIVE PLANT

TERMS AND CONDITIONS

This load of concrete is produced in accordance with the A.S.T.M. standard specifications for Redi-Mix concrete.

We do not guarantee finished results obtained from this load of concrete, as many important factors affecting the ultimate quality of the completed job are out of our control.

Excessive water in concrete reduces its final strength. Any water added to the mix on the job will be at the purchaser's risk.

Ready Mix concrete is not returnable for credit.

In the event of delivery beyond curb line, this company will not assume liability for damage to curbs, sidewalks, driveways or other personal property.

Estimated delivery schedules will be maintained to the best of our ability. We will not consider any claims for damages for failure to do so.

Customer will be allowed 6 minutes per yard unloading time. Overtime price will apply to any additional time.

Water added: _____

Gallons _____

Customer's representative _____

CUSTOMER ID	P.O. NUMBER	ZONE	JOB NUMBER	TIME	DATE	TICKET
NA0002				2:33 PM	17-Oct-14	54939
SOLD TO VERN NAGEL			DELIVER TO HALEY TO CLINTON GO W LOOK FOR JACK NAPOLEON 6"SL AFTER FLAKE			

QUANTITY THIS LOAD	QUANTITY ORDERED	QUANTITY DELIVERED	PRODUCT CODE	PRODUCT DESCRIPTION	UNIT OF MEASURE	UNIT PRICE	EXTENDED PRICE
2.50	7.50	7.50	67FS	JMPWC10W750 CLASS FS	yd		
1.00	1.00	1.00	940	DELIVERY CHARGE	ea		
TRUCK					SUB-TOTAL		
KELSEY	PLANT	SLUMP	DUE AT JOB	USE OF CONCRETE	TAX		
	PVILLE	4.00			TOTAL		
CALCIUM					AIR ENTRAIN		
SUPER PLAS.					ACCELERATOR		

DELIVERY INSTRUCTIONS

SPECIAL INSTRUCTIONS

TEAR HERE

Truck	Driver	User	Disp	Ticket Num	Ticket ID	Time	Date
77	KELSEY	user		54939		14:33	10/17/14
Load Size	Mix Code	Returned	Qty	Mix Age	Seq	Load ID	
2.50 yd	67FS				D	60373	
Material	Design Qty	Required	Batched	% Var	Moisture	Actual Wet	
57-CUS7	1470 lb	3703 lb	3650 lb	-1.16%	0.75% M	3 gal	
SMS-HSO	490 lb	2552 lb	2540 lb	-0.45%	3.00% M	9 gal	
LAF-TYP1	900 lb	2250 lb	2210 lb	-2.67%			
PRO-CONAIR	2.00 /C	45.00 ac	45.00 ac	0.00%			
Water #1	39.0 gal	55.0 gal	55.0 gal	0.00%		55.0 gal	
Actual New Batches: 1							
Load Total: 6972 lb Design W/C: 0.362 Water/Cement: 0.352 T Design Waters: 97.5 gal Actual Waters: 67.4 gal To Add: 0.1 gal							
Slump: 4.00 in Adjust Water: 0.0 gal/Load Trim Water: 0.0 gal/yd							



Pettisville • Stony Ridge • McClure

M&R REDI-MIX, INC.

READY MIXED CONCRETE • AGGREGATE
SUPPLIES • CUSTOM TRUCKING
(800) 786-6325

521 Commercial Street
Pettisville, OH 43553
PH: (419) 445-7771

5601 Cherry Street
Stony Ridge, OH 43463
PH: (800) 786-6325

MAILING ADDRESS
BOX 53038
PETTISVILLE, OHIO 43553

L-207 Rd. 1-C
McClure, OH 43534
PH: (419) 748-8442

TERMS AND CONDITIONS

CAUTION

May cause eye or skin injury. Contains Portland cement. Freshly mixed cement, mortar, concrete, or grout may cause skin injury.

TAKE THESE PRECAUTIONS:

- Avoid all contact with eyes.
- Wear rubber boots and gloves, and avoid prolonged contact directly with skin or through porous materials.
- In case of contact with skin or eyes. FLUSH THOROUGHLY WITH WATER.
- If irritation persists, get medical attention promptly.
- Keep children away.

This load of concrete is produced in accordance with the A.S.T.M. standard specifications for Redi-Mix concrete.

We do not guarantee finished results obtained from this load of concrete, as many important factors affecting the ultimate quality of the completed job are out of our control.

Excessive water in concrete reduces its final strength. Any water added to the mix on the job will be at the purchaser's risk.

Ready Mix concrete is not returnable for credit.

In the event of delivery beyond curb line, this company will not assume liability for damage to curbs, sidewalks, driveways or other personal property.

Estimated delivery schedules will be maintained to the best of our ability. We will not consider any claims for damages for failure to do so.

Customer will be allowed 6 minutes per yard unloading time. Overtime price will apply to any additional time.

Water added:

Gallons

Customer's representative

CUSTOMER ID	P.O. NUMBER	ZONE	JOB NUMBER	TIME	DATE	TICKET
5002				1:42 PM	17-Oct-14	54936
VERN NAGEL			HALEY TO CLINTON GO W		LOOK FOR JACK	
			NAPOLEON 6"SL AFTER FLAKE			

QUANTITY THIS LOAD	QUANTITY ORDERED	QUANTITY DELIVERED	PRODUCT CODE	PRODUCT DESCRIPTION	UNIT OF MEASURE	UNIT PRICE	EXTENDED PRICE
5.00	5.00	5.00	67FS	JMF#C100790 CLASS FS	yd		
TRUCK	PLANT	SLUMP	DUE AT JOB	USE OF CONCRETE	SUB-TOTAL		
CALCIUM JOE	AIR ENTRAIN	SUPER PLAS.	ACCELERATOR		TAX		
					TOTAL		

DELIVERY INSTRUCTIONS

SPECIAL INSTRUCTIONS

TEAR HERE

Truck	Driver	User	Disp	Ticket	Num	Ticket ID	Time	Date			
91	JOE	user				54936	13:42	10/17/14			
Load Size	Mix Code	Returned	Qty	Mix	Age	Seq	Load ID				
5.00 yd	67FS					D	60369				
Material	Design Qty	Required	Batched	% Var	Moisture	Actual Wat					
57-CUST	1470 lb	7406 lb	7360 lb	-0.61%	0.75% M	7 gl					
2NS-HSG	100 lb #	515 lb	470 lb	-8.82%	3.00% M	2 gl					
LAF-TYP1	900 lb	4500 lb	4510 lb	0.22%							
PRO-CONAIR	2.20 /C	90.00 oz	90.00 oz	0.00%							
Water #1	39.0 gal	161.5 gal	161.0 gal	-0.30%		161.0 gl					
Actual	Num Batches:	2									
Load Total:	13689 lb	Design W/C:	0.362	Water/Cement:	0.361 T	Design Water:	195.0 gl	Actual Water:	169.3 gl	To Add:	0.7 gl
Slump:	4.00 in	Adjust Water:	0.0 gl	Load Trim Water:	0.0 gl	yd					

The Sand Shark



FINLEY HAULING & EXCAVATING

P.O. Box 2807
Whitehouse, Ohio 43571
(419) 875-4169 Phone/Fax

HOURLY TICKETS

110 4194

Date 10-16-14

Job Contractor Vern Nagel

Job Name & Address Clinton St

Material Hauled DIRT

Broker's Name _____

Driver's Name & Truck No. Teresa Hermichauer #16

Start Time 7:00

Lunch _____

Finish Time 4:00

Total Hours 9

Circle One

Tandem

Tri-axle

Quad

Quin

Foreman's Signature [Signature]



FINLEY
HAULING & EXCAVATING

P.O. Box 2807
Whitehouse, Ohio 43571
(419) 875-4169 Phone/Fax

HOURLY TICKETS

110 4186

Date 10/16/14

Job Contractor NASEL

Job Name & Address CLINTON ST.

Material Hauled DIRT

Broker's Name _____

Driver's Name & Truck No. BIL FH 14

Start Time 7:00

Lunch _____

Finish Time 3:15

Total Hours 8 1/4

Circle One

Tandem

Tri-axle

Quad

Quin

Foreman's Signature [Signature]
